

CONTRACTOR'S SUBMITTAL TRANSMITTAL

City of Rancho Palos Verdes

DATE: 6/12/2017

PROJECT TITLE: RPV Storm Drain Improvements FY 16-17; Project No. 021817

WORK ORDER No. 021817

CONSTRUCTION MANAGER: Natalie Chan

DATE RECEIVED: _____

DRAWING REFERENCE: _____

<p>TO:</p> <p style="text-align: center;">City of Rancho Palos Verdes Attn: Natalie Chan 30940 Hawthorne Blvd Rancho Palos Verdes, CA 90275</p> <p>P: 310.544.5252 F: 310.544.5292</p>	<p>CONTRACTOR'S SUBMITTAL NO.: 1.0</p> <p>CHECK ONE:</p> <p><input checked="" type="checkbox"/> An original submittal.</p> <p><input type="checkbox"/> A 2nd Submittal</p> <p><input type="checkbox"/> A 3rd Submittal</p> <p><input type="checkbox"/> An O&M submittal</p>
<p>FROM: <i>COLICH & Sons, L.P.</i> 547 W. 140th Street Gardena, CA 90248</p> <p style="text-align: center;">Chris Heidel - Project Manager P: (310) 516-6346 F: (310) 217-2573</p>	

ITEM NO.	*	SUBJECT OF SUBMITTAL	COPIES	SPECIFICATION SECTION(S)	SUPPLIER
1		Baseline Schedule			


* CHECK FOR SPECIFIED SHOP INSPECTION REQUIREMENT, FOR ITEM SOURCE GREATER THAN 50 MILES, ATTACH LABORATORY DOCUMENTATION FOR ACCEPTANCE.

COMPLETE EITHER (a) OR (b):

a) We have verified that the material or equipment contained in this submittal meets all requirements specified or shown (no exceptions).

b) We have verified that the material or equipment contained in this submittal meets all requirements specified or shown, except for the following deviations:

NOTES / COMMENTS:

	<p>AUTHORIZED CONTRACTOR'S REPRESENTATIVE:</p>  Chris Heidel - Project Manager Date: 6/12/2017
--	---

Project: S. D. Improvements Project No. 021817
 Agency: City of Rancho Palos Verdes
 Contractor: Colich & Sons, L.P.
 Contract Duration: 60 Work Days
 Start Date: 8/3/17 Completion Date: 10/26/17

Preliminary Construction Schedule


ID	Task Name	Duration	Start	Finish	Predecessors	Jun 11, '17							Jun 18, '17							Jun 25, '17							Jul 2, '17							Jul 9, '17							Jul 16, '17							Jul 23, '17							Jul 30, '17						
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
1	Colich Submittals - Pipe, etc	10 days	Mon 6/12/17	Fri 6/23/17		[Task Bar]																																																							
2	Submittal Review - City	10 days	Fri 6/23/17	Thu 7/6/17									[Task Bar]																																																
3	Manufacture RCP Pipe	20 days	Fri 7/7/17	Thu 8/3/17																[Task Bar]																																									
4	Resident Notifications	10 days	Tue 7/25/17	Mon 8/7/17																							[Task Bar]																																		
5	Caltrans - Double Permit	15 days	Thu 7/6/17	Wed 7/26/17																[Task Bar]																																									
6	Mobilization - Line C	3 days	Thu 8/3/17	Mon 8/7/17																							[Task Bar]																																		
7	Pothole Utilities	2 days	Thu 8/3/17	Fri 8/4/17																														[Task Bar]																											
8	Install Mainline RCP	12 days	Mon 8/7/17	Tue 8/22/17																																					[Task Bar]																				
9	Install Laterals	6 days	Mon 8/14/17	Mon 8/21/17																																					[Task Bar]																				
10	Install Concrete Structures	12 days	Wed 8/9/17	Thu 8/24/17																																					[Task Bar]																				
11	Restore Permanent Paving	6 days	Thu 8/17/17	Thu 8/24/17																																					[Task Bar]																				
12	Demobilize Line C Site	2 days	Thu 8/24/17	Fri 8/25/17																																					[Task Bar]																				
13	Mobilization - Line D	2 days	Mon 8/28/17	Tue 8/29/17																																					[Task Bar]																				
14	Pothole Utilities	2 days	Fri 8/25/17	Mon 8/28/17																																					[Task Bar]																				
15	Install Mainline RCP	15 days	Tue 8/29/17	Mon 9/18/17																																					[Task Bar]																				
16	Install Laterals	5 days	Thu 9/7/17	Wed 9/13/17																																					[Task Bar]																				
17	Install Concrete Structures	10 days	Mon 9/11/17	Fri 9/22/17																																					[Task Bar]																				
18	Restore Permanent Paving	4 days	Tue 9/19/17	Fri 9/22/17																																					[Task Bar]																				
19	Restore Easements	6 days	Fri 9/15/17	Fri 9/22/17																																					[Task Bar]																				
20	Demobilize Line D Site	2 days	Thu 9/21/17	Fri 9/22/17																																					[Task Bar]																				
21	Mobilize - Line D5	2 days	Fri 9/22/17	Mon 9/25/17																																					[Task Bar]																				
22	Pothole Utilities	2 days	Mon 9/25/17	Tue 9/26/17																																					[Task Bar]																				
23	Install Mainline RCP	3 days	Tue 9/26/17	Thu 9/28/17																																					[Task Bar]																				
24	Install Concrete Structures	3 days	Wed 9/27/17	Fri 9/29/17																																					[Task Bar]																				
25	Restore Permanent Paving	2 days	Fri 9/29/17	Mon 10/2/17																																					[Task Bar]																				
26	Demobilize Line D5 Site	1 day	Tue 10/3/17	Tue 10/3/17																																					[Task Bar]																				
27	Mobilize - Line B & B2	2 days	Thu 9/28/17	Fri 9/29/17																																					[Task Bar]																				
28	Pothole Utilities	3 days	Fri 9/29/17	Tue 10/3/17																																					[Task Bar]																				
29	Install Mainline - Line B	6 days	Tue 10/3/17	Tue 10/10/17																																					[Task Bar]																				
30	Install Concrete Structures	8 days	Mon 10/9/17	Wed 10/18/17																																					[Task Bar]																				
31	Install Laterals	3 days	Mon 10/16/17	Wed 10/18/17																																					[Task Bar]																				
32	Install Mainline - Line B2	4 days	Wed 10/11/17	Mon 10/16/17																																					[Task Bar]																				
33	Install Laterals	3 days	Mon 10/16/17	Wed 10/18/17																																					[Task Bar]																				
34	Install Concrete Structures	5 days	Tue 10/17/17	Mon 10/23/17																																					[Task Bar]																				
35	Restore Permanent Paving	5 days	Wed 10/18/17	Tue 10/24/17																																					[Task Bar]																				
36	Demobilize Line B & B2 Site	3 days	Mon 10/23/17	Wed 10/25/17																																					[Task Bar]																				

Project: RPV Baseline Schedule
 Date: Mon 6/12/17

Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone

Project: S. D. Improvements Project No. 021817
 Agency: City of Rancho Palos Verdes
 Contractor: Colich & Sons, L.P.
 Contract Duration: 60 Work Days
 Start Date: 8/3/17 Completion Date: 10/26/17

Preliminary Construction Schedule

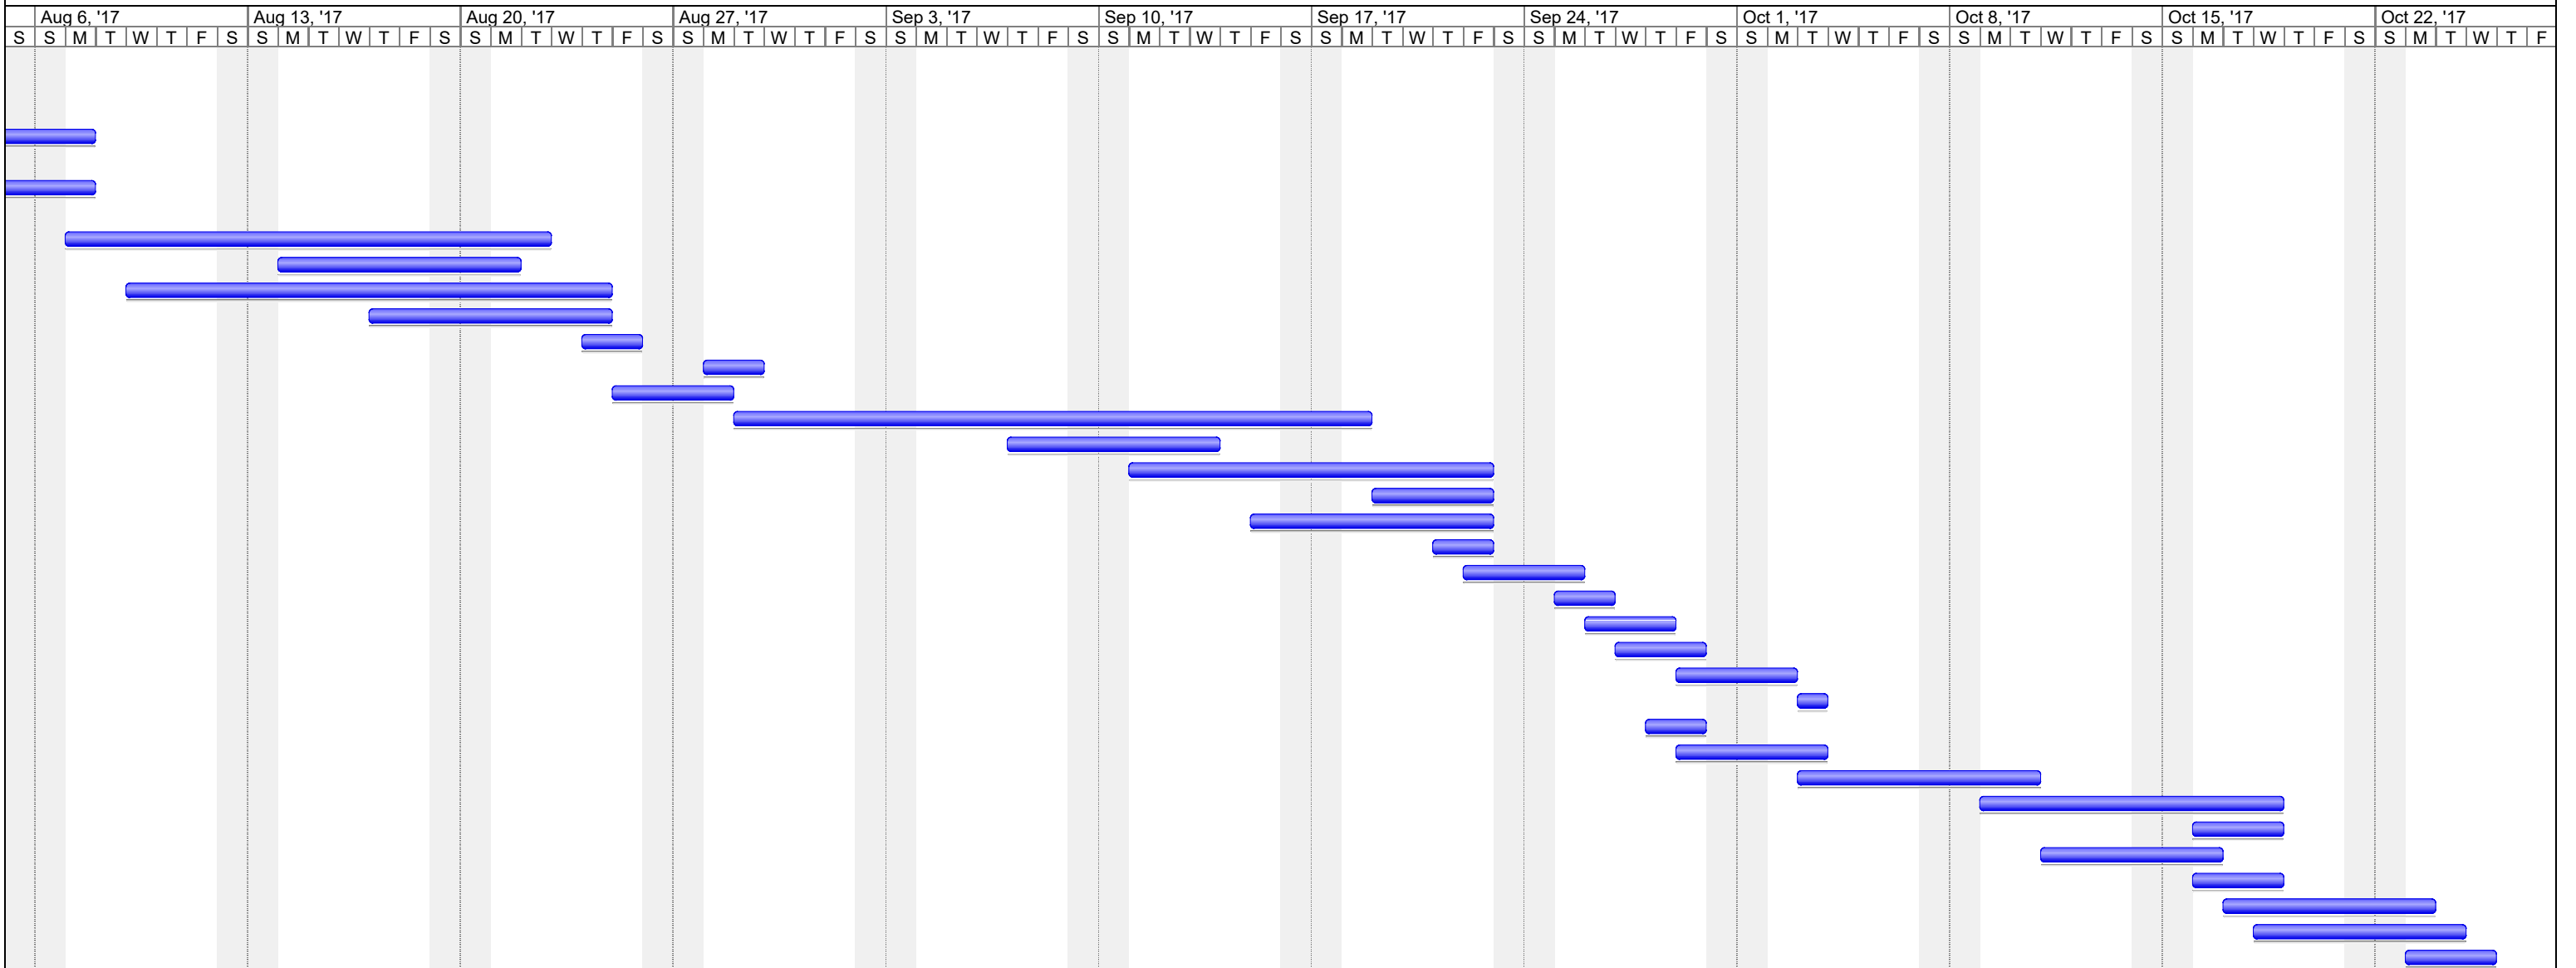

Project: RPV Baseline Schedule
 Date: Mon 6/12/17

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
